

EXECUTIVE SUMMARY REPORT

SUN PRAIRIE ELEMENTARY SCHOOLS: Token Springs Elementary School 03/30/2018

What's New?

A lot of progress was made at Token Springs this week, both on the exterior and the interior. The exterior canopies received blocking so that they can receive metal panels in the upcoming weeks. On the inside, bathroom floor tile is being installed in the first floor bathrooms, and fluid-applied flooring is being installed in the kitchen. Once those floors are in, the bathroom accessories and the kitchen equipment will be installed! In the gym, the acoustic wall panels are being painted and will be hung in the coming weeks. The ELRC, art room, and library are framed out with steel studs, and they will be drywalled and painted in the coming weeks!

The Past Weeks

- Finished framing the art room and library areas
- Installed cubbies and sliding glass walls in the 4th/5th grade wing
- Fluid-applied flooring received in the kitchen
- Painted the cafeteria ceiling
- Bathroom ceramic floor tile in the cafeteria bathroom and k/1st grade wing

Coming Up in the Weeks Ahead

- Finish steel stud framing and start hanging drywall in the ELRC
- Carpet and Resilient Flooring in the grade wings
- Start installing acoustical wall panels and basketball hoops in the gym
- Begin hanging drywall in the art room and library
- Paint and install casework in the administration offices




MEP rough-ins are progressing nicely in the ELRC as the area gets ready for drywall soon.



Ceiling grid is being dropped in the kindergarten/1st grade wing, adding some nice color to the classrooms!



The exterior canopies are drywalled and have been sprayed with the air-vapor barrier, so they are now ready to receive metal panels!

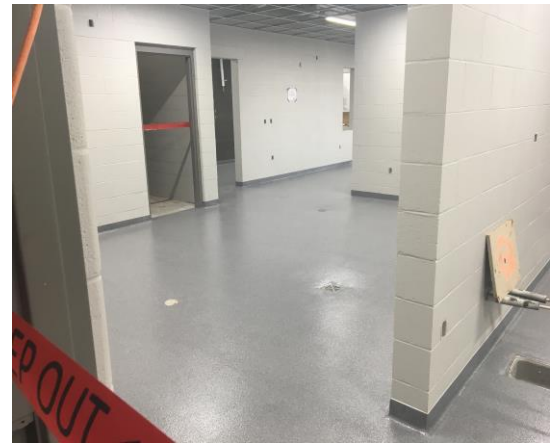

Fluid-applied cementitious flooring was installed in the kitchen this week. Once it dries, the kitchen equipment will be installed.



Did you know? In the kitchen, the flooring that is being installed is an polyurethane-based cementitious flooring. The purpose of this flooring is to be resistant to grease, mold and leaks, allowing for the floor to last a long time without needing replacement, as well as making it easy to clean. The floor is "fluid applied", meaning that it is applied as a liquid and spread evenly over the floor to a thickness of about 4mm. It then cures for 5 days before being ready to use. The end result is a durable floor that looks great and keeps the kitchen clean!

EXECUTIVE SUMMARY REPORT

SUN PRAIRIE ELEMENTARY SCHOOLS

03/30/2018



The cafeteria ceiling was painted this week and drywall will be installed on the soffits next week.



The drywallers will be busy next week because the library and art room walls are completely framed and ready to be drywalled!



On the outside of the gym walls, the metal panels are installed and looking sleek! Now that the gym is finished, there are only a few spots left on the school that need metal paneling!



Our plumbers are all smiles as they see the progress that Token Springs Elementary is making!!
